Secrt. II-48—22,202—6-2-23.

L.S.G (1923) Department.

M

Dois SERIES.

G.O. No. 1332 L&m

DATED 9 — 6 — 1923

[Despatch Abstract.]

Grant - road - trunk - Hospet Municipality - Maintenance druing 1922-23 - Rs. 2179 sanctioned.

C.F. 31.

Public Works **DEPARTMENT.**

In future letters, please quote No. 939 dated 5/1/23 and short title *

Rec'd ..... Enclosures .....

Reg'd ..... Spare copies .....

Telephone No.
Post Box No.
Telegraphic Address:

Dated 30th January 1923. 192 .

From (Name) M.F. Kharegat Esq., A.M.I.C.E.,
(Designation) Superintending Engineer, III Circle
(Address) Bellary.

To The Chief Engineer,
Public Works Department,
MADRAS.

Sir,

Trunk Roads in Hospet Municipality.
Annual inspection made by the Superintending Engineer, for the year 1922-23.

C.C. No. 415 L & M., dated 4th March 1921.

I have the honour to report on the portion of the Madras-Bombay Trunk Road in Hospet Municipal limits 2 miles 2 furlongs 38th/6 - 40th/7.

Renewals have been done again in the 39th mile and it is in good order. Renewals had also been done in the first two furlongs of the 40th mile, and patch repairs in other places. There is a considerable improvement in the standard of work this year. The road is cut up and requires repairs from 40/2 to the toll gate.

Some earthwork in widening the berms in the 39th and 40th mile has been done. The lead for earthwork is said to be 4 furlongs and the rate paid including watering and consolidation Rs. 19/- per unit. This is excessive, a rate of Rs. 16-12-0 should be sufficient. In the 40th mile there are about 3 furlongs where banks on the side berms between the avenue trees are found. These might well be utilised leaving a sufficient amount of earth round the trees if necessary. Instead of bringing earth for such a distance to make up berms the side drains could be widened and deepened except actually in the village where they would be

would be dangerous. Rs. 112/- have been spent on sign boards but the names have not yet been painted on them.

Rs. 2,098/- have been spent against the estimate provision of Rs. 2,250/- .

The full grant may be given to the Municipality for 1922-23.

5/2/23

Superintending Engineer, III Circle,

Bellary.

K.R. 1/2/23.

P.W.D. V-59 (a)—16,632—4-8-20.

Data sheet to accompany the estimate for Trunk Roads in Hospet Municipality

Quantity.	Description of work.	Rate. RS.	A.	P.	Per	Amount. RS.	A.	P	Total.
1000 cft.	Excavating hard soil. clay or shale as per item No. 26	4	2	0	1000 cft	4	2	0	
1000 cft.	Cartage ~~00~~ 4 furlongs	1	1	7	1000 cft.	10	16	10	
1000 cft.	Watering & consolidation as per No. 33 c.	1	8	0	1000 cft.	1	8	0	
	Sundries.				—	0	2	2	
						16	12	0	16-12-0

Rec
1/2/23

C.F. No. 64,264 - 4-4 21.

DEPARTMENT.



Received ... 192 *Registered* 12086 192

Subject.

Grnats:- Trunk Road. Hospet Municipality.

ENCLOSURES.
No. One.
Spare copies ..

C.R.No. 619-Accta of 1921.

Station Hospet , *Dated the* 14 th day of May 1923 .

From (Name) M.R.Ry. Devan Bahdur T.Kothandaram Naidu Garu,

(Designation) Chairman Muni cipal Council .
Hospet

To The Secretary to the Government of Madras,
Local and Muni dipal ---Department.
Madras.

Sir,

I have the honour to submit herewith a statement/ showing the total expenditure incurred on the trunk road ---- during 1922-23 as desired in Government Memo No 10357-1-L.M. dated 4-5-1923.

I have the honour to be
Sir,
Your most obedient servant.

Chairman

15/5/23.

1575

Municipal Office. Hospet.

Dated 14-5-1923.

T R U N K R O A D:- 2 Miles and 2 Furlongs.

1 Total expenditure incurred on road(excluding charges on account of establishment , tools & Plant).....Rs 2016/-.

2 Value of metal collected but not spread:..... Nil.

3 Net expenditure on roads:..... 2016/-.

4 Add per centage charges on item No 3 (for establishment 10 % and----------Rs 202/-
and for tools and plant 1½ % ..... 30/-.....) 232/.

Total:.....Rs 2248/.

5. Total grant payable subject to the maximum of Rs 1000/- per mile in the case of roads in charge of Municipal Councils.....Rs 2500/-.

Chairman.

15/5/23.

4 / Pwd

: Mtg

(15)

DS

Submitted that the S.E's report may be sent to S.T for an Sw. & S.E. SE's recommendation accepted

C.T.A
9/5

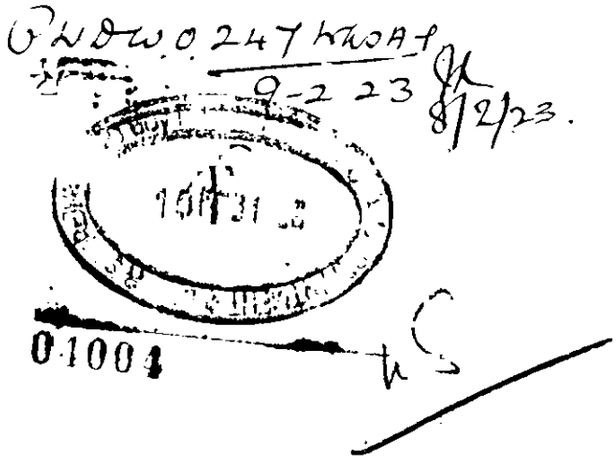

K.S.S.

L.S.G

Name of trunk road - Madras-Bombay road.

Length - m 2 f 1 yds 95

Maximum grant permissible Rs 2179.

Please see statement on page 5 of Bk. The Sup. Engineer and the Chief Engineer recommend the payment of the maximum grant. A draft order (sanctioning the grant is) submitted for appl. - It may be sent to finance for acceptance

Weaver 25/5 L.S.P.

KB 20.5.23

ASSISTANT SECRETARY TO GOVT. FINANCE DEPARTMENT. 28 MAY 1923

Lee 24.5.23. LSG 23/5

Fin

m 4004-1 Lom 28.5.23.

Tmd 39513 I KBI 28/5/23 RTW

P T O

2/

Finance Dept

The draft order may be accepted.

All
4-6-23.

CRS
7.6.23

H.H.S.

Item 3915 BE-1
86-23



Scott. II-1a (a)—48,962—2-2-22. (6)

PWD DEPARTMENT

	Date.	Initials.
When received for Fair-copying.		
When copied ..		
When examined ..	11/6	
When signed ..		
When despatched ..		

READ AGAIN G.O. No. ....., dated ..... 192 .

" " " " ....., " ..... 192 .

READ ALSO;—

C. No. 12086, From the Chc Hospet. No 619, dated 16.5.1923.

" " ..... " " ....., " ..... 192 .

" " ..... " " ....., " ..... 192 .

ORDER.

The

No 1332 dated 9-6-1923.

The inspection notes of the Sup. Engineer on the trunk road in the Hospet municipality are communicated to the Muni Council.

2 The Govt are pleased to sanction a grant of (which is the maximum grant admissible) Rs 2179/ to the Hospet Muni Council towards the expenditure incurred by it on trunk roads in 1922-23. The Accts General is requested to

place the amount at the disposal of the municipal Council at an early date. The amount will be met from the provision of Rs 15.41 lakhs in the CBE for the current year under 41 A Civil Works - Grants in aid - Contributions - Grants to local bodies for the maintenance of trunk roads.

CBE

KB 19/5/23

PW 23/5/23

DESPATCHED
1 JUN 1923

To The Chief Engineer
(with a copy of the SE's memorandum)
.. Collr of Bellary
.. P. Wks
.. Finance Dept
.. A.G
.. Examr of C.F.
Accts

Copy to Secretariat
